

Assignment No #2.

Course: Project Management


Name: Abdul Haseeb

ID: 16744.

Q1: Use the data in this table to answer the question

Activity	Preceding Activity	Estimate in Month
start		0
D	start	4
A	start	6
F	D, A	7
E	D	8
G	F, E	5
B	F	5
H	G	7
C	H	8
End	C, B	0

Solution:

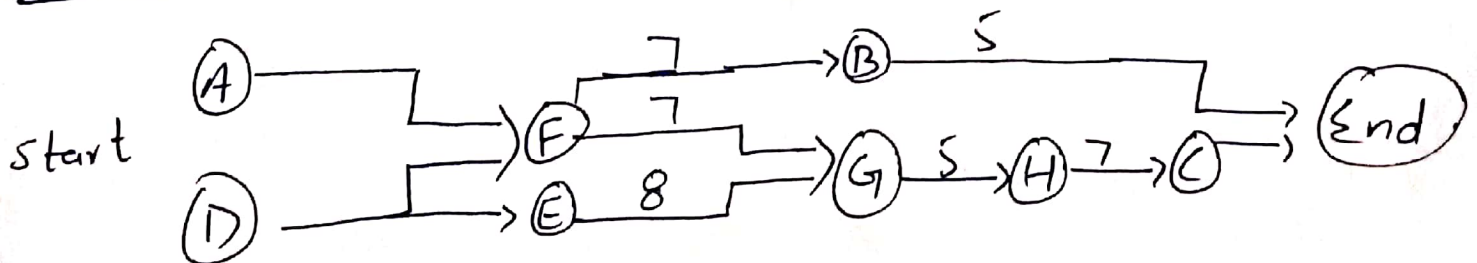

Critical Path = $G + 7 + 5 = 18$ Month.

Critical Path = $A - F - B = 18$ Month.
